
DEMO Enterprise Platform — real-data live rollout

How the demo becomes the system Alderbrook Group runs on every day, with real people, real pay and real books. Nine steps, four checkpoints. Nothing goes live until its checkpoint says **Yes**.

130	≈ 6½	3	Apr 30, 2027
WORKING DAYS	MONTHS	GO-LIVE WAVES	ALL LIVE

⚠ **Before day 1:** the current demo link and Netlify copy keep data in the web browser with demo sign-in and illustrative payroll. **Never type real names, SINs, bank details or pay into them.** Real data only goes into the real system built in step 3.

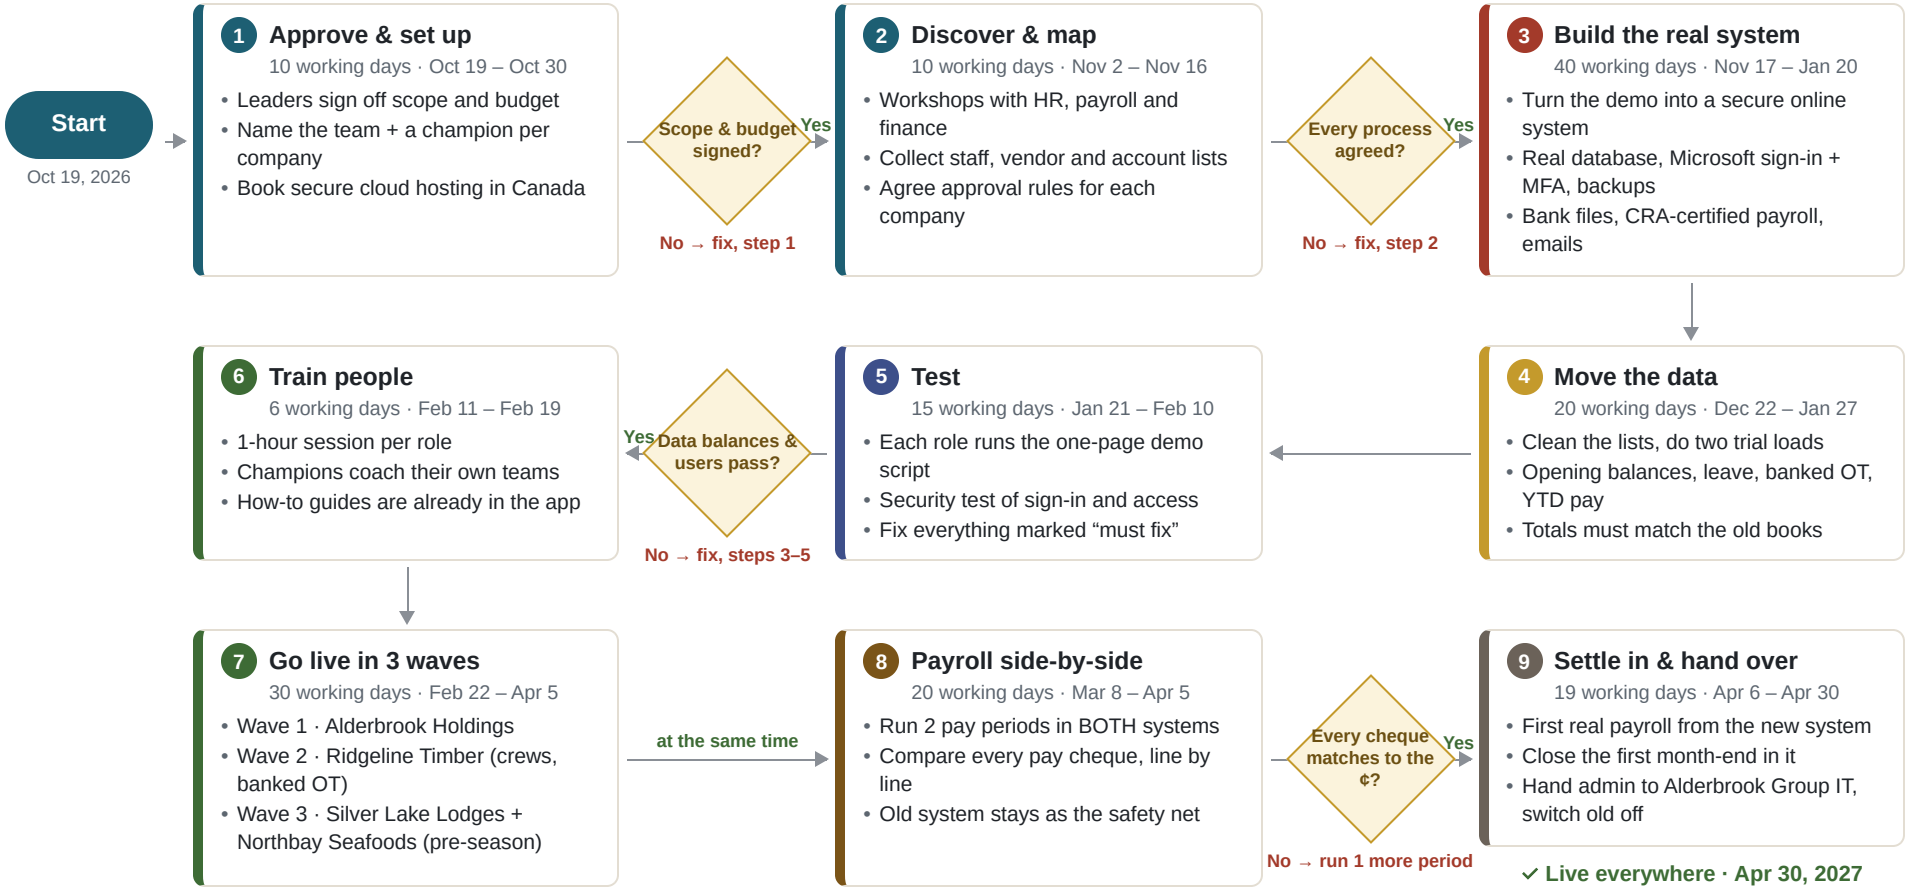


Checkpoint — must be “Yes” to move on · Plan · Build · Data · Test · People & go-live · Payroll

Working days = Mon–Fri, without BC stat holidays and a Dec 24 – Jan 1 closure. Start Oct 19, 2026. The waves follow the four companies; the demo can also be shown as one company (Alderbrook Holdings with the same eight departments, people and approvals), chosen on its first page.

Timeline — Oct 19, 2026 to Apr 30, 2027

Bars are working days. Steps 3 and 4 overlap; go-live waves run while payroll is checked side-by-side. First real payroll: pay period starting **Apr 12, 2027**.

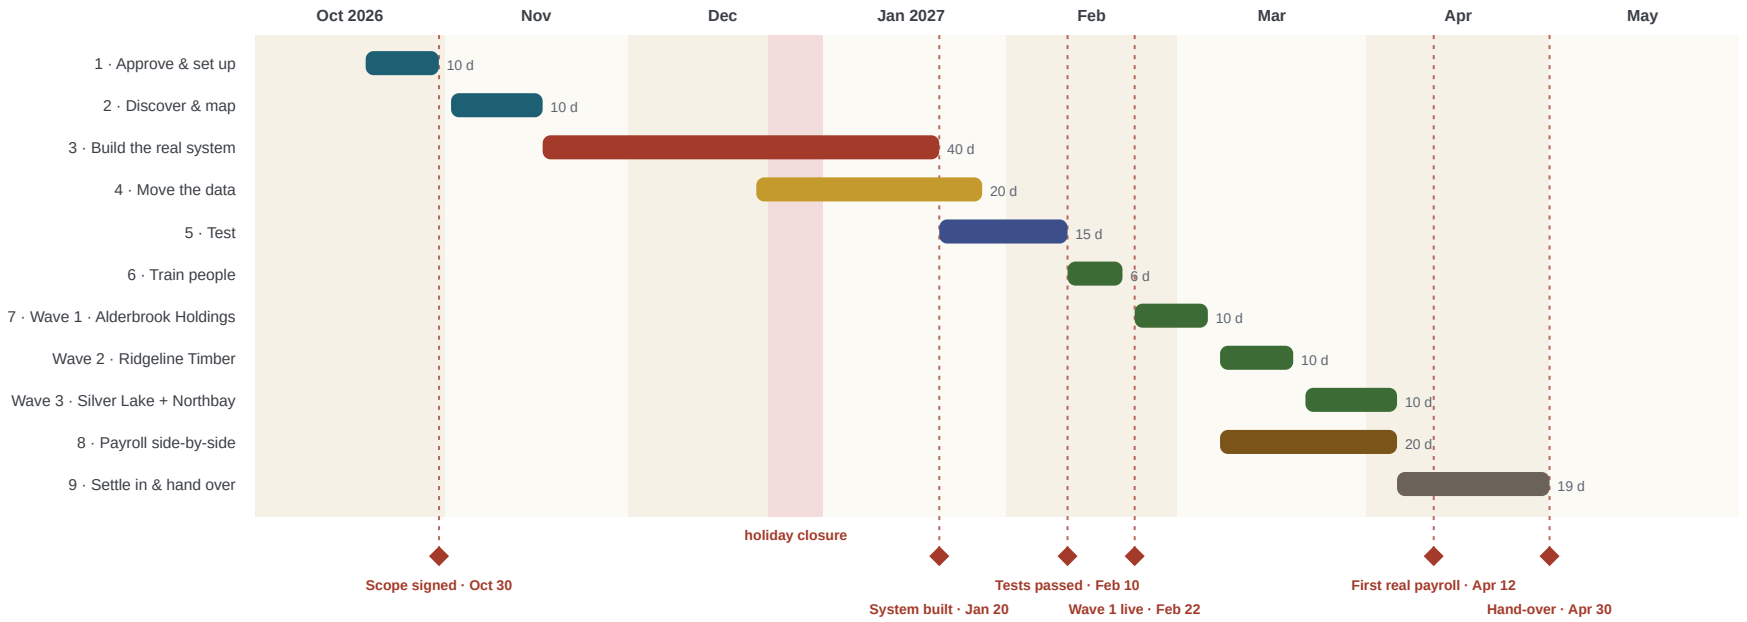

How long will it take?

OPTION	DAYS	ALL LIVE BY
Fast track — HR, time, requests, purchasing, finance; keep today's payroll provider for now	≈ 95	Mar 11, 2027
Recommended — everything in the demo, including payroll	**130**	**Apr 30, 2027**
Solo build — you build alone (no second developer); step 3 takes twice as long	≈ 170	Jun 28, 2027

Assumes a project lead (you), 1–2 developers, and HR, payroll and finance leads giving about 1 day a week. Add 15–20% buffer for surprises.

Who you need

- **Sponsor** (CEO) — signs off checkpoints, clears roadblocks
- **Project lead** (you) — plan, weekly status, go / no-go calls
- **Developers** (1–2) — build, data loads, fixes
- **HR lead** — staff records, leave, benefits, pension
- **Payroll lead** — rates, deductions, side-by-side runs
- **Finance lead** — chart of accounts, vendors, opening balances
- **IT / security** — Microsoft sign-in, hosting, backups
- **Champion per company** — Alderbrook, Ridgeline, Silver Lake, Northbay

Biggest risks — and the fix

- **Wrong pay.** Use CRA-certified payroll formulas; go live only after 2 pay runs match the old system to the cent.
- **Messy data.** Two trial loads; totals must match the old books before go-live.
- **Privacy.** Hosting in Canada, MFA, role-based access, audit log (BC PIPA).
- **Busy season.** Silver Lake Lodges and Northbay Seafoods go live in March, before their season.
- **Mid-year payroll switch.** Carry year-to-date totals across so T4s are right.
- **People don't adopt it.** Champions, 1-hour role training, in-app how-to guides.
